





ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB  
62 PRINCE STREET, CRONULLA NSW 2230  
DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023



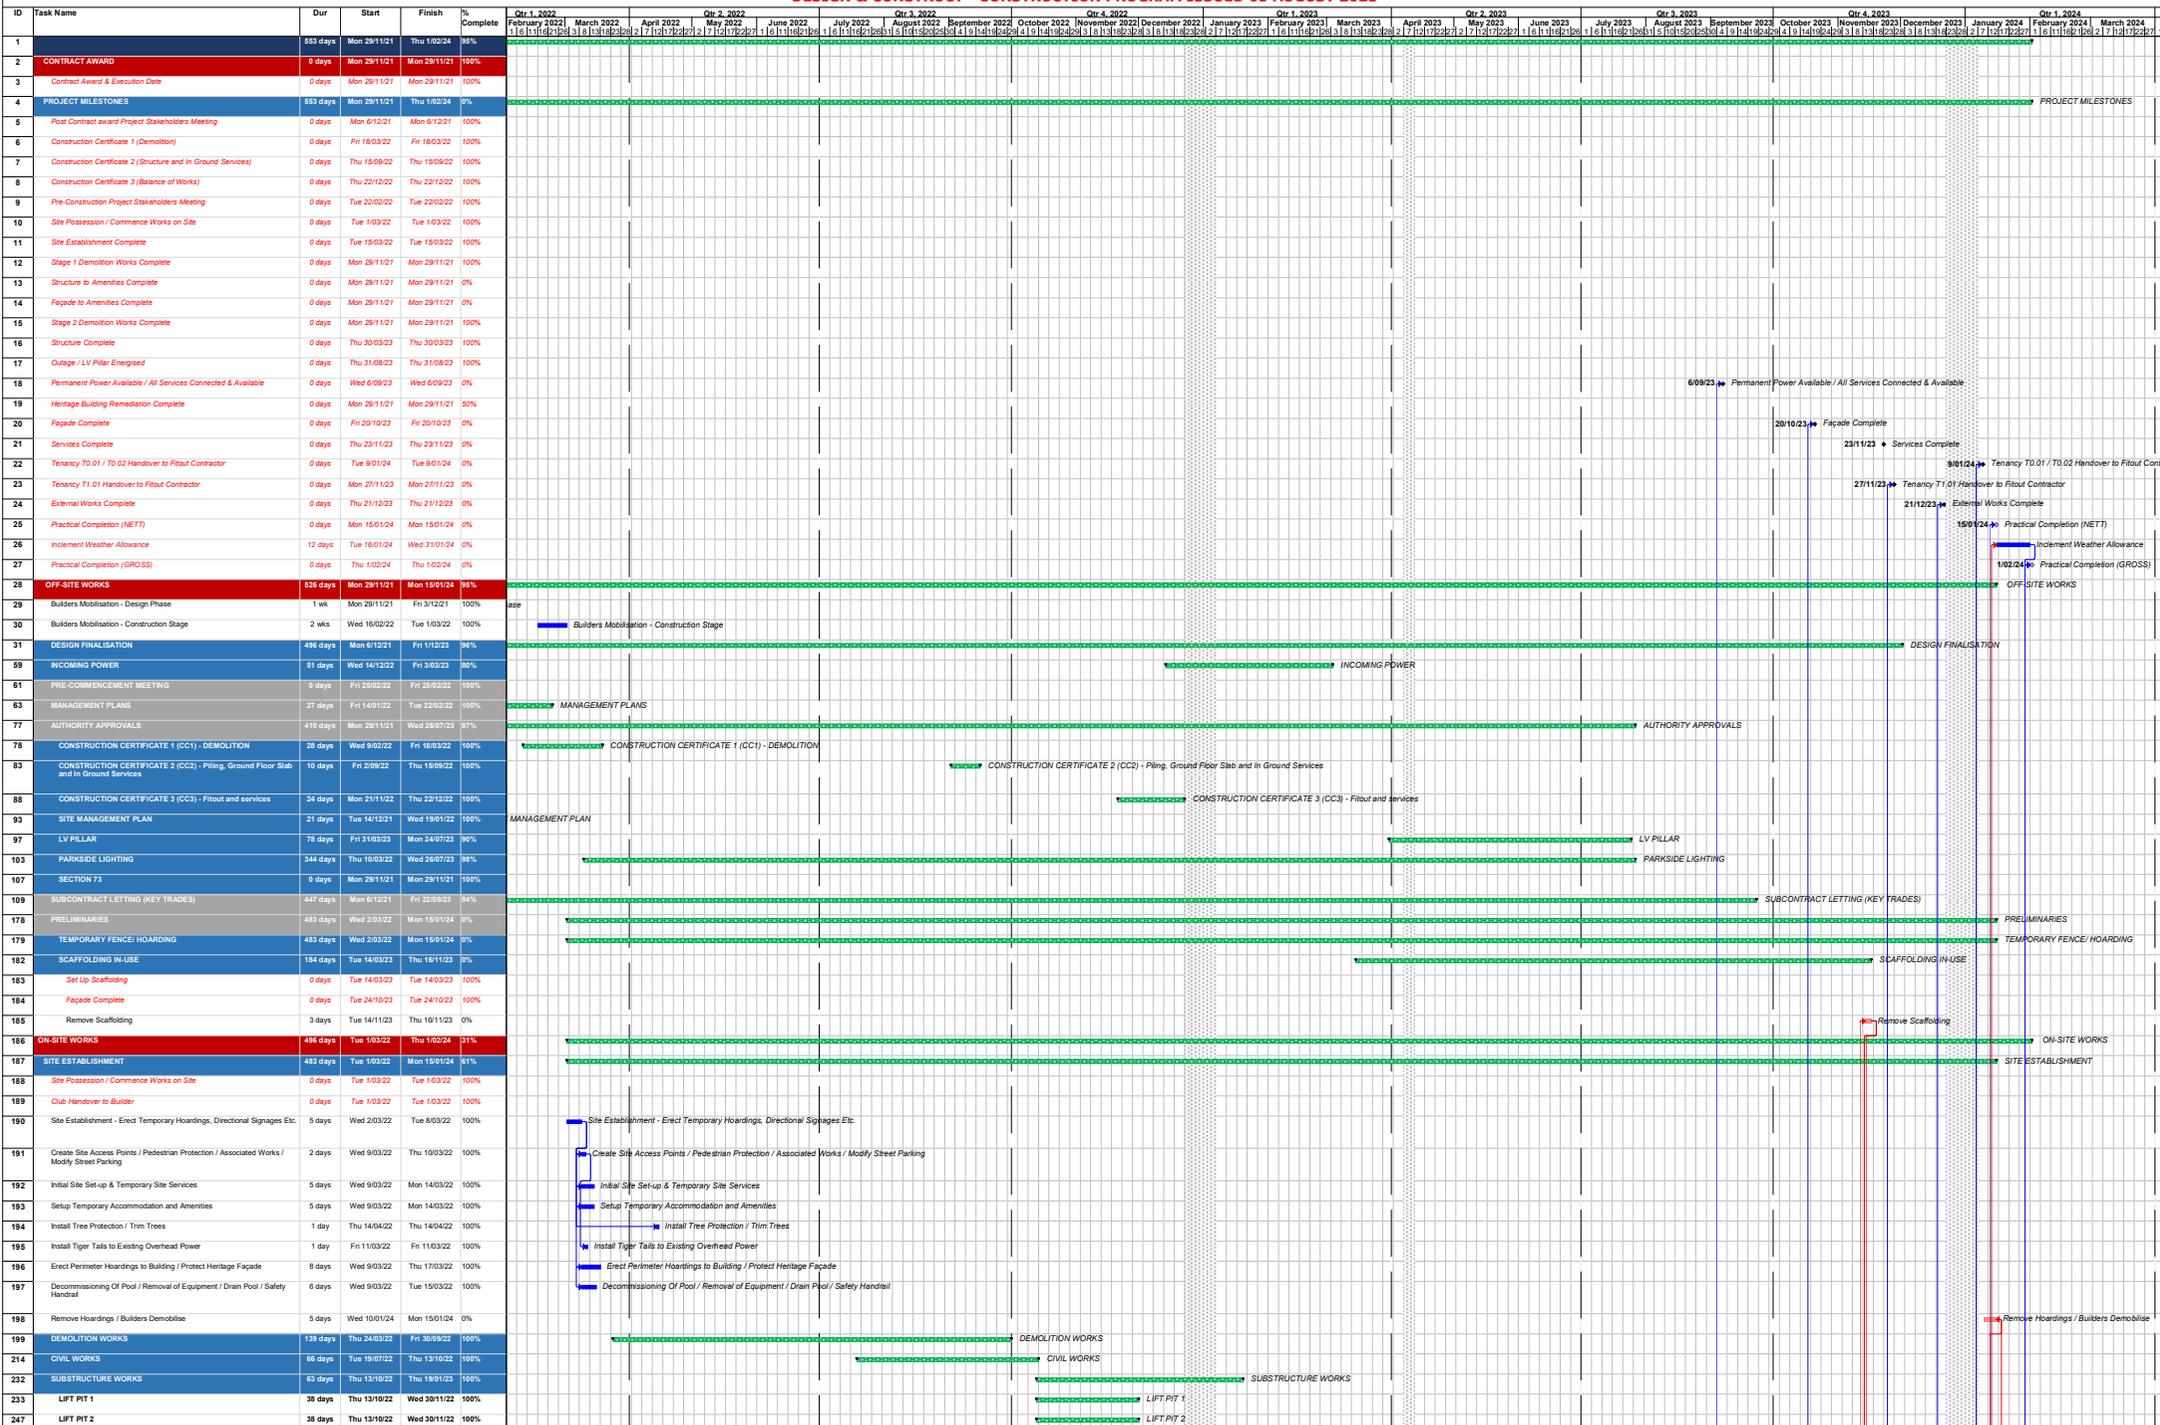


ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB  
62 PRINCE STREET, CRONULLA NSW 2230  
DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023

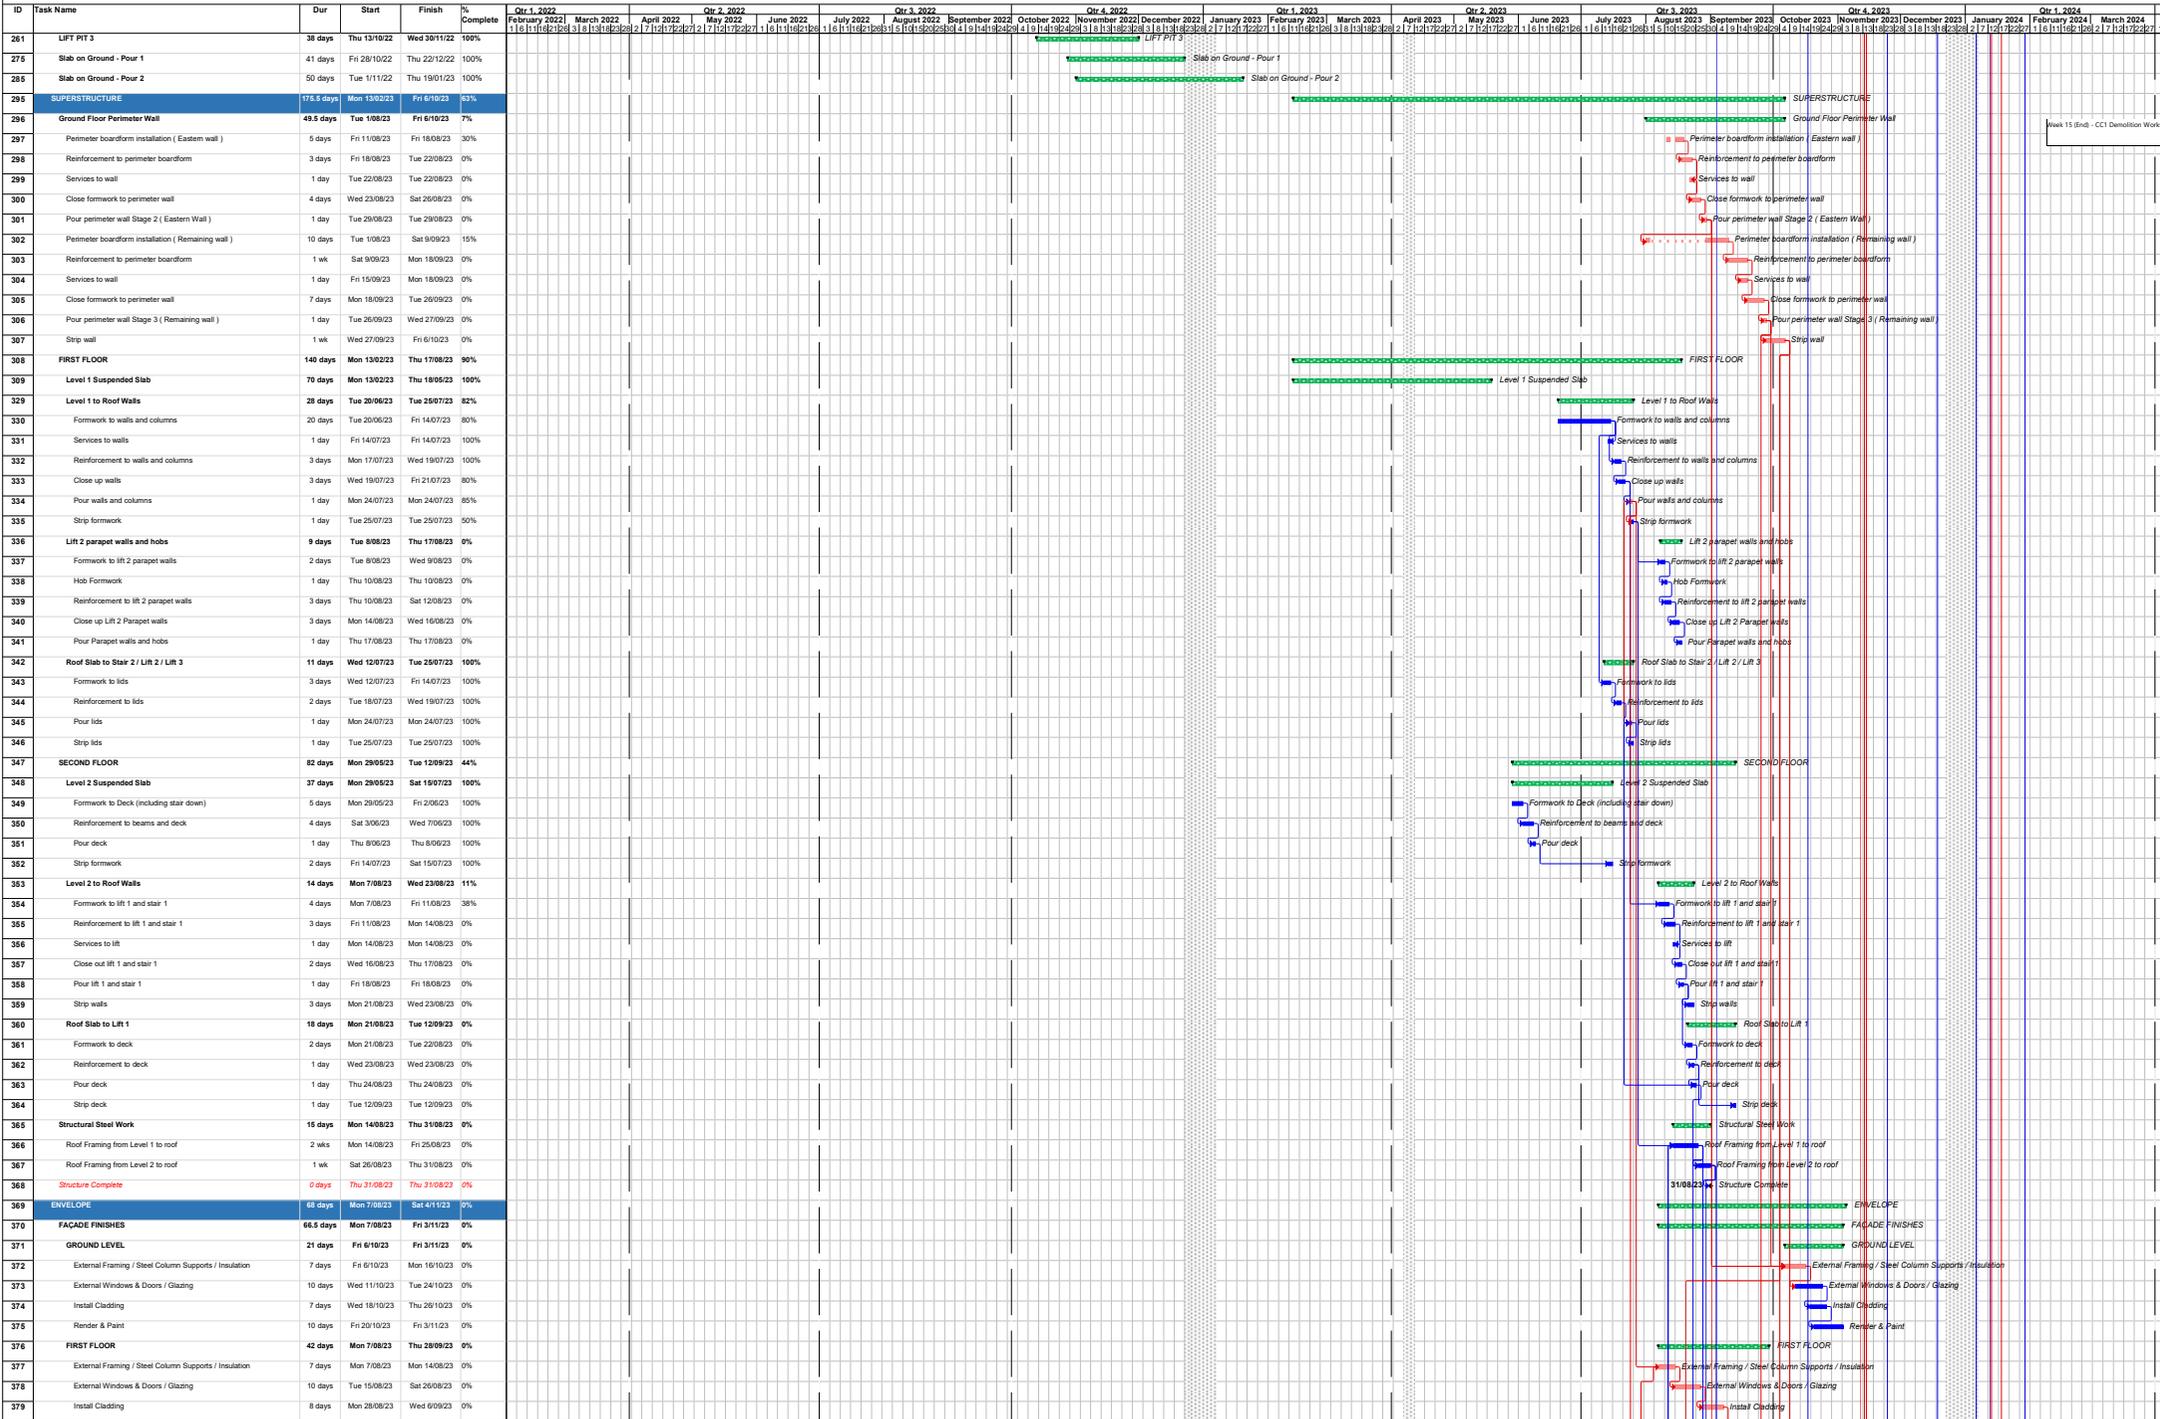




ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB  
62 PRINCE STREET, CRONULLA NSW 2230  
DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023

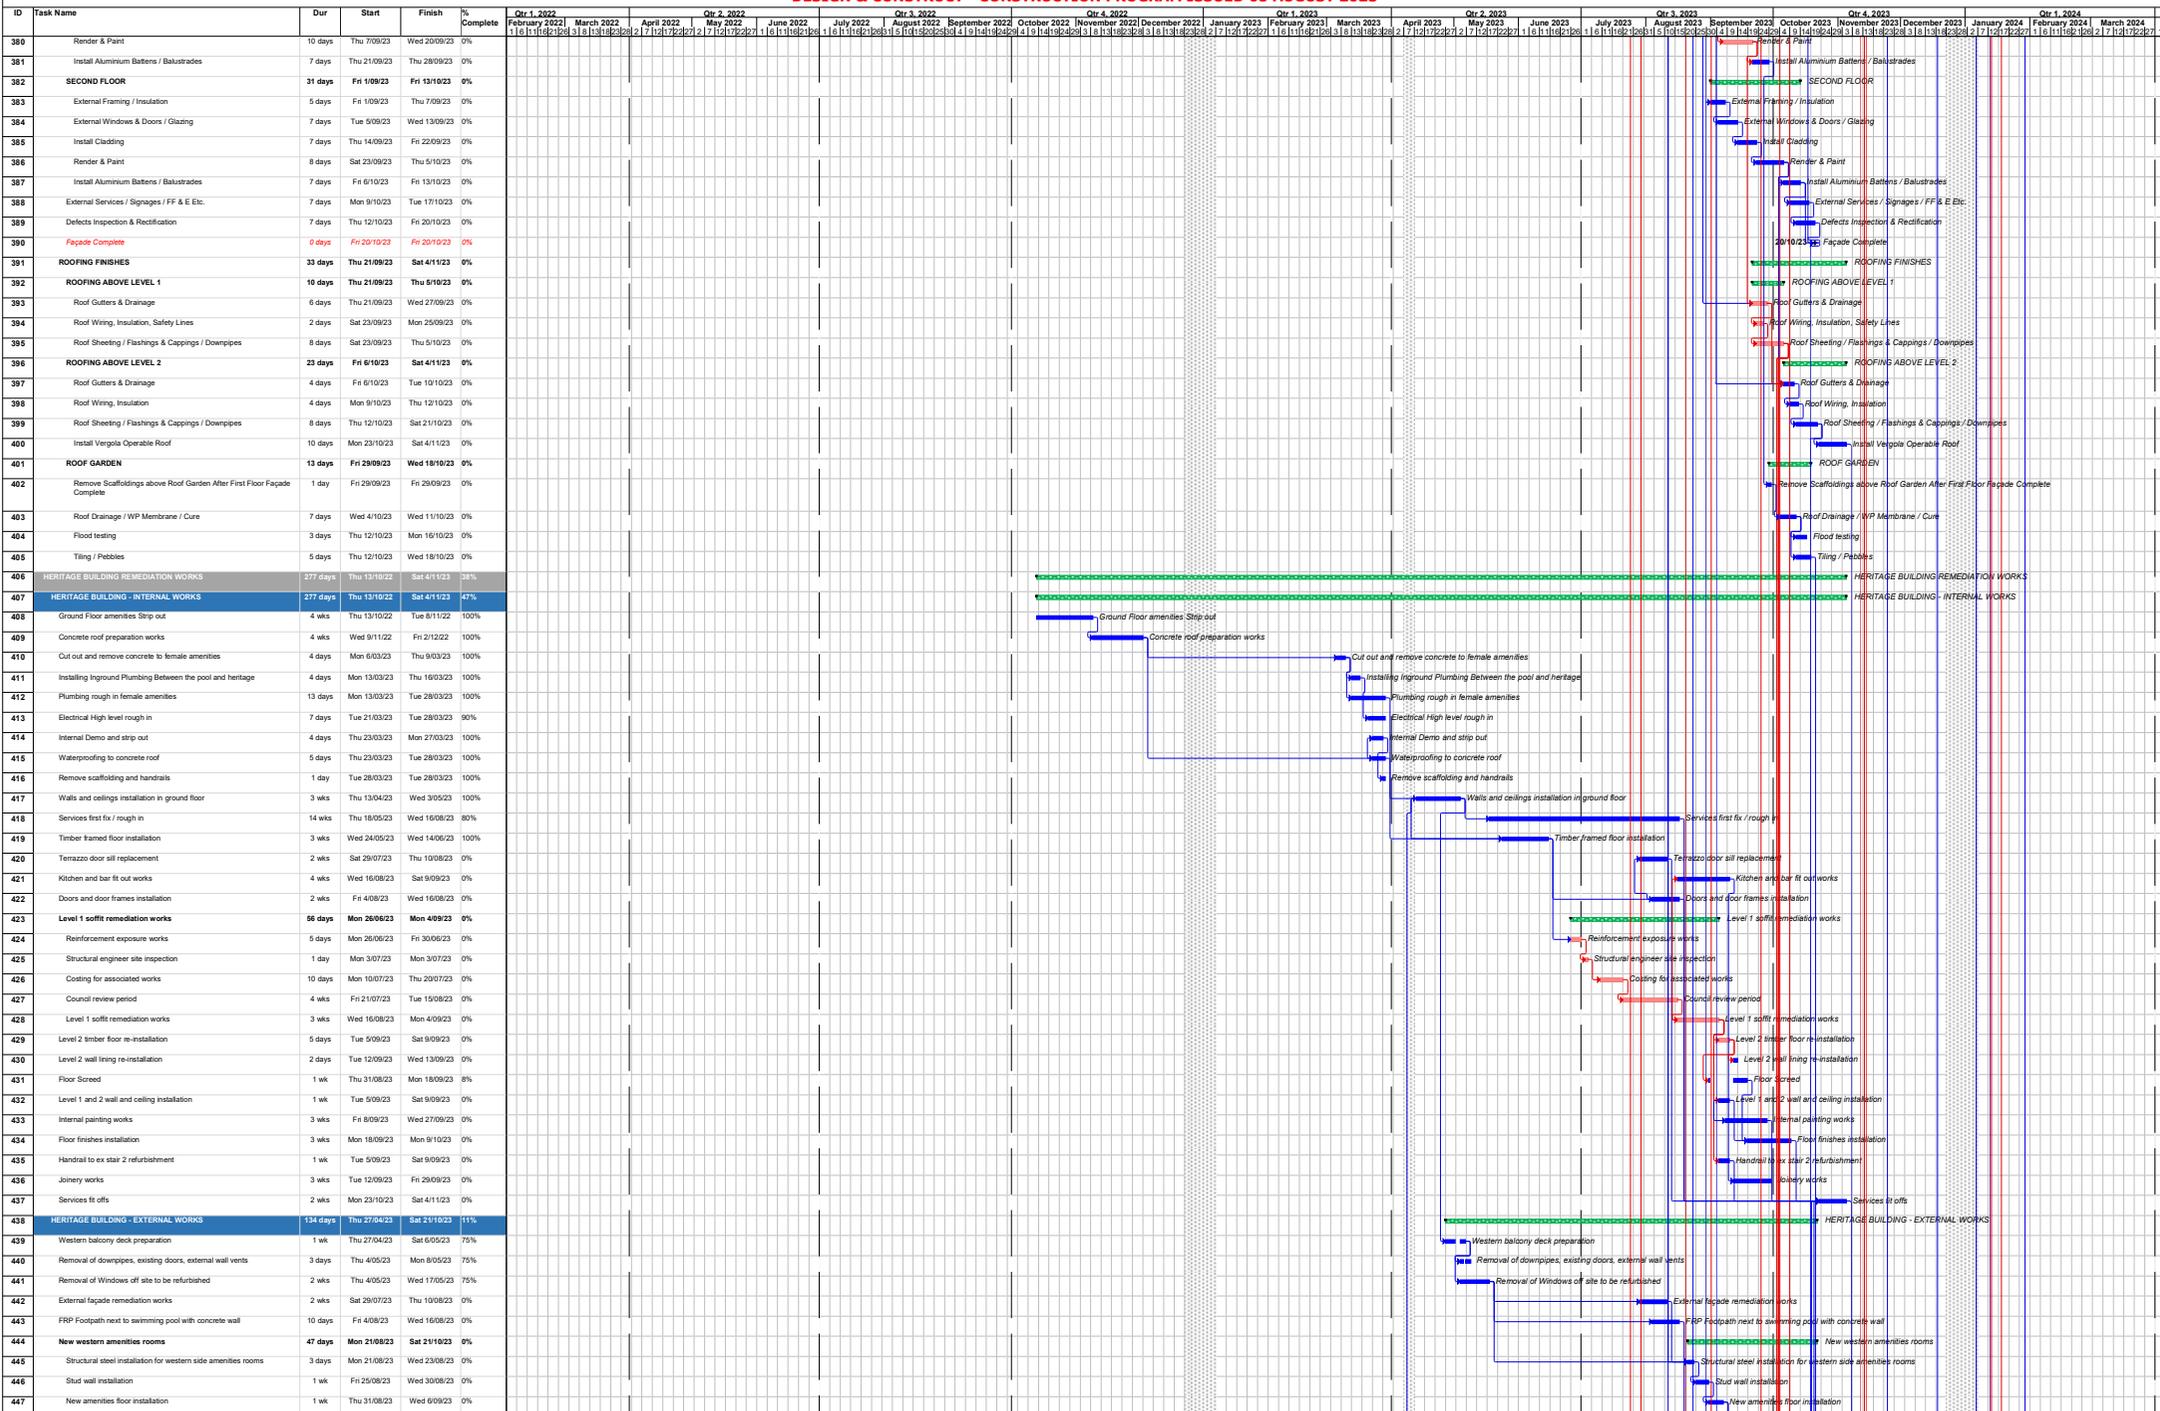




**ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB  
62 PRINCE STREET, CRONULLA NSW 2230  
DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023**

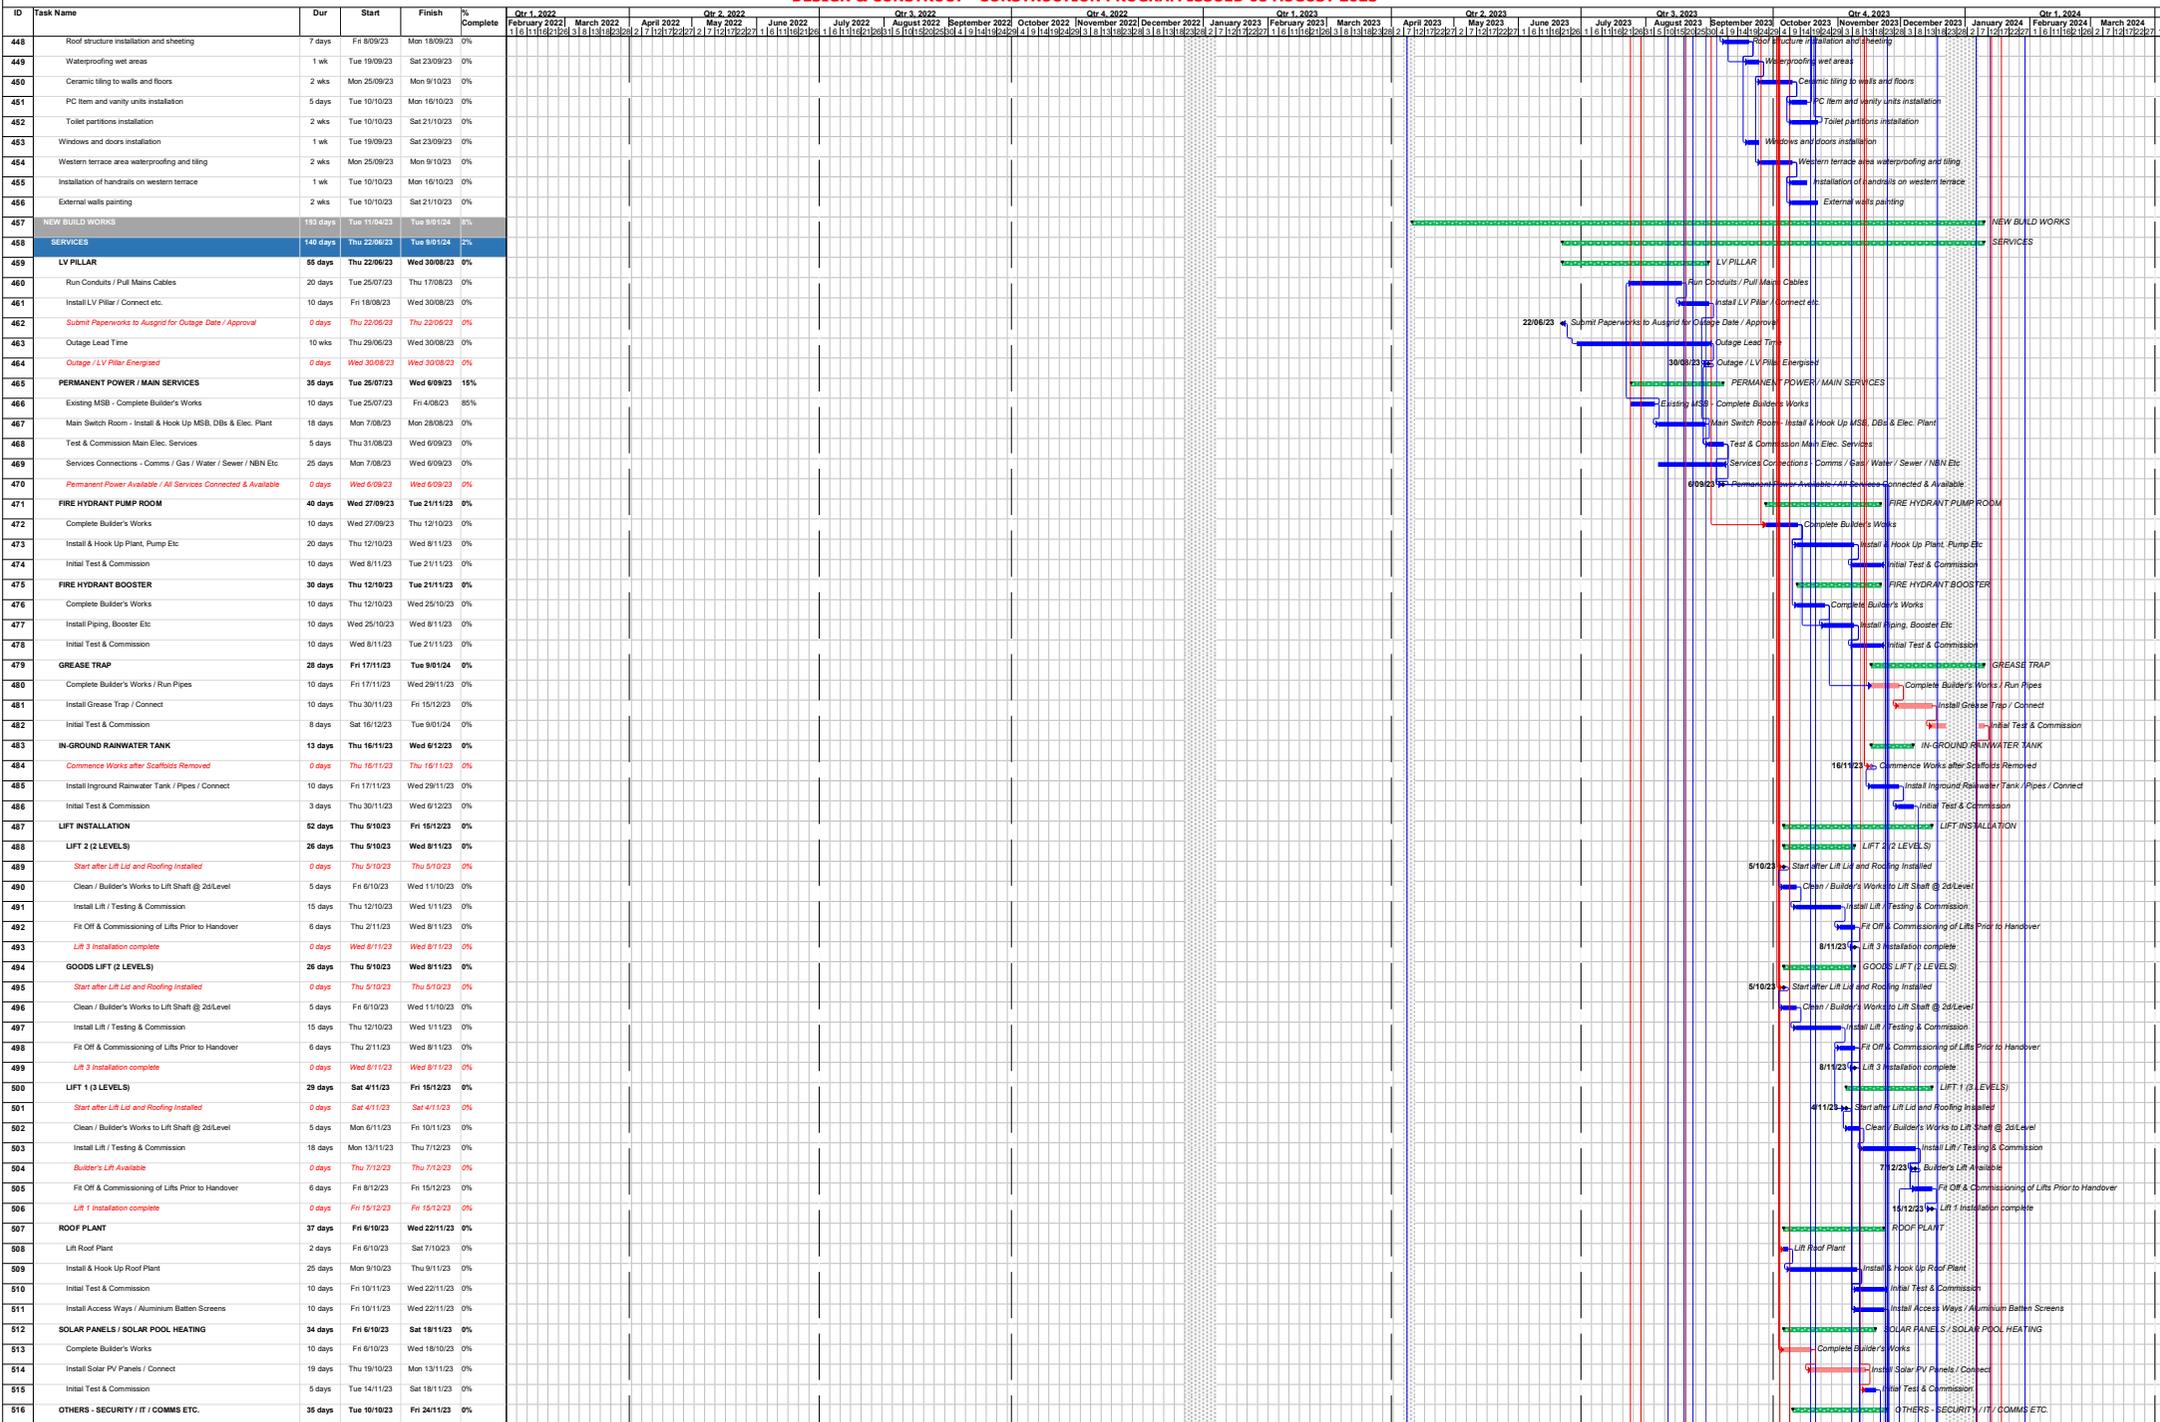



**ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB**  
**62 PRINCE STREET, CRONULLA NSW 2230**  
**DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023**

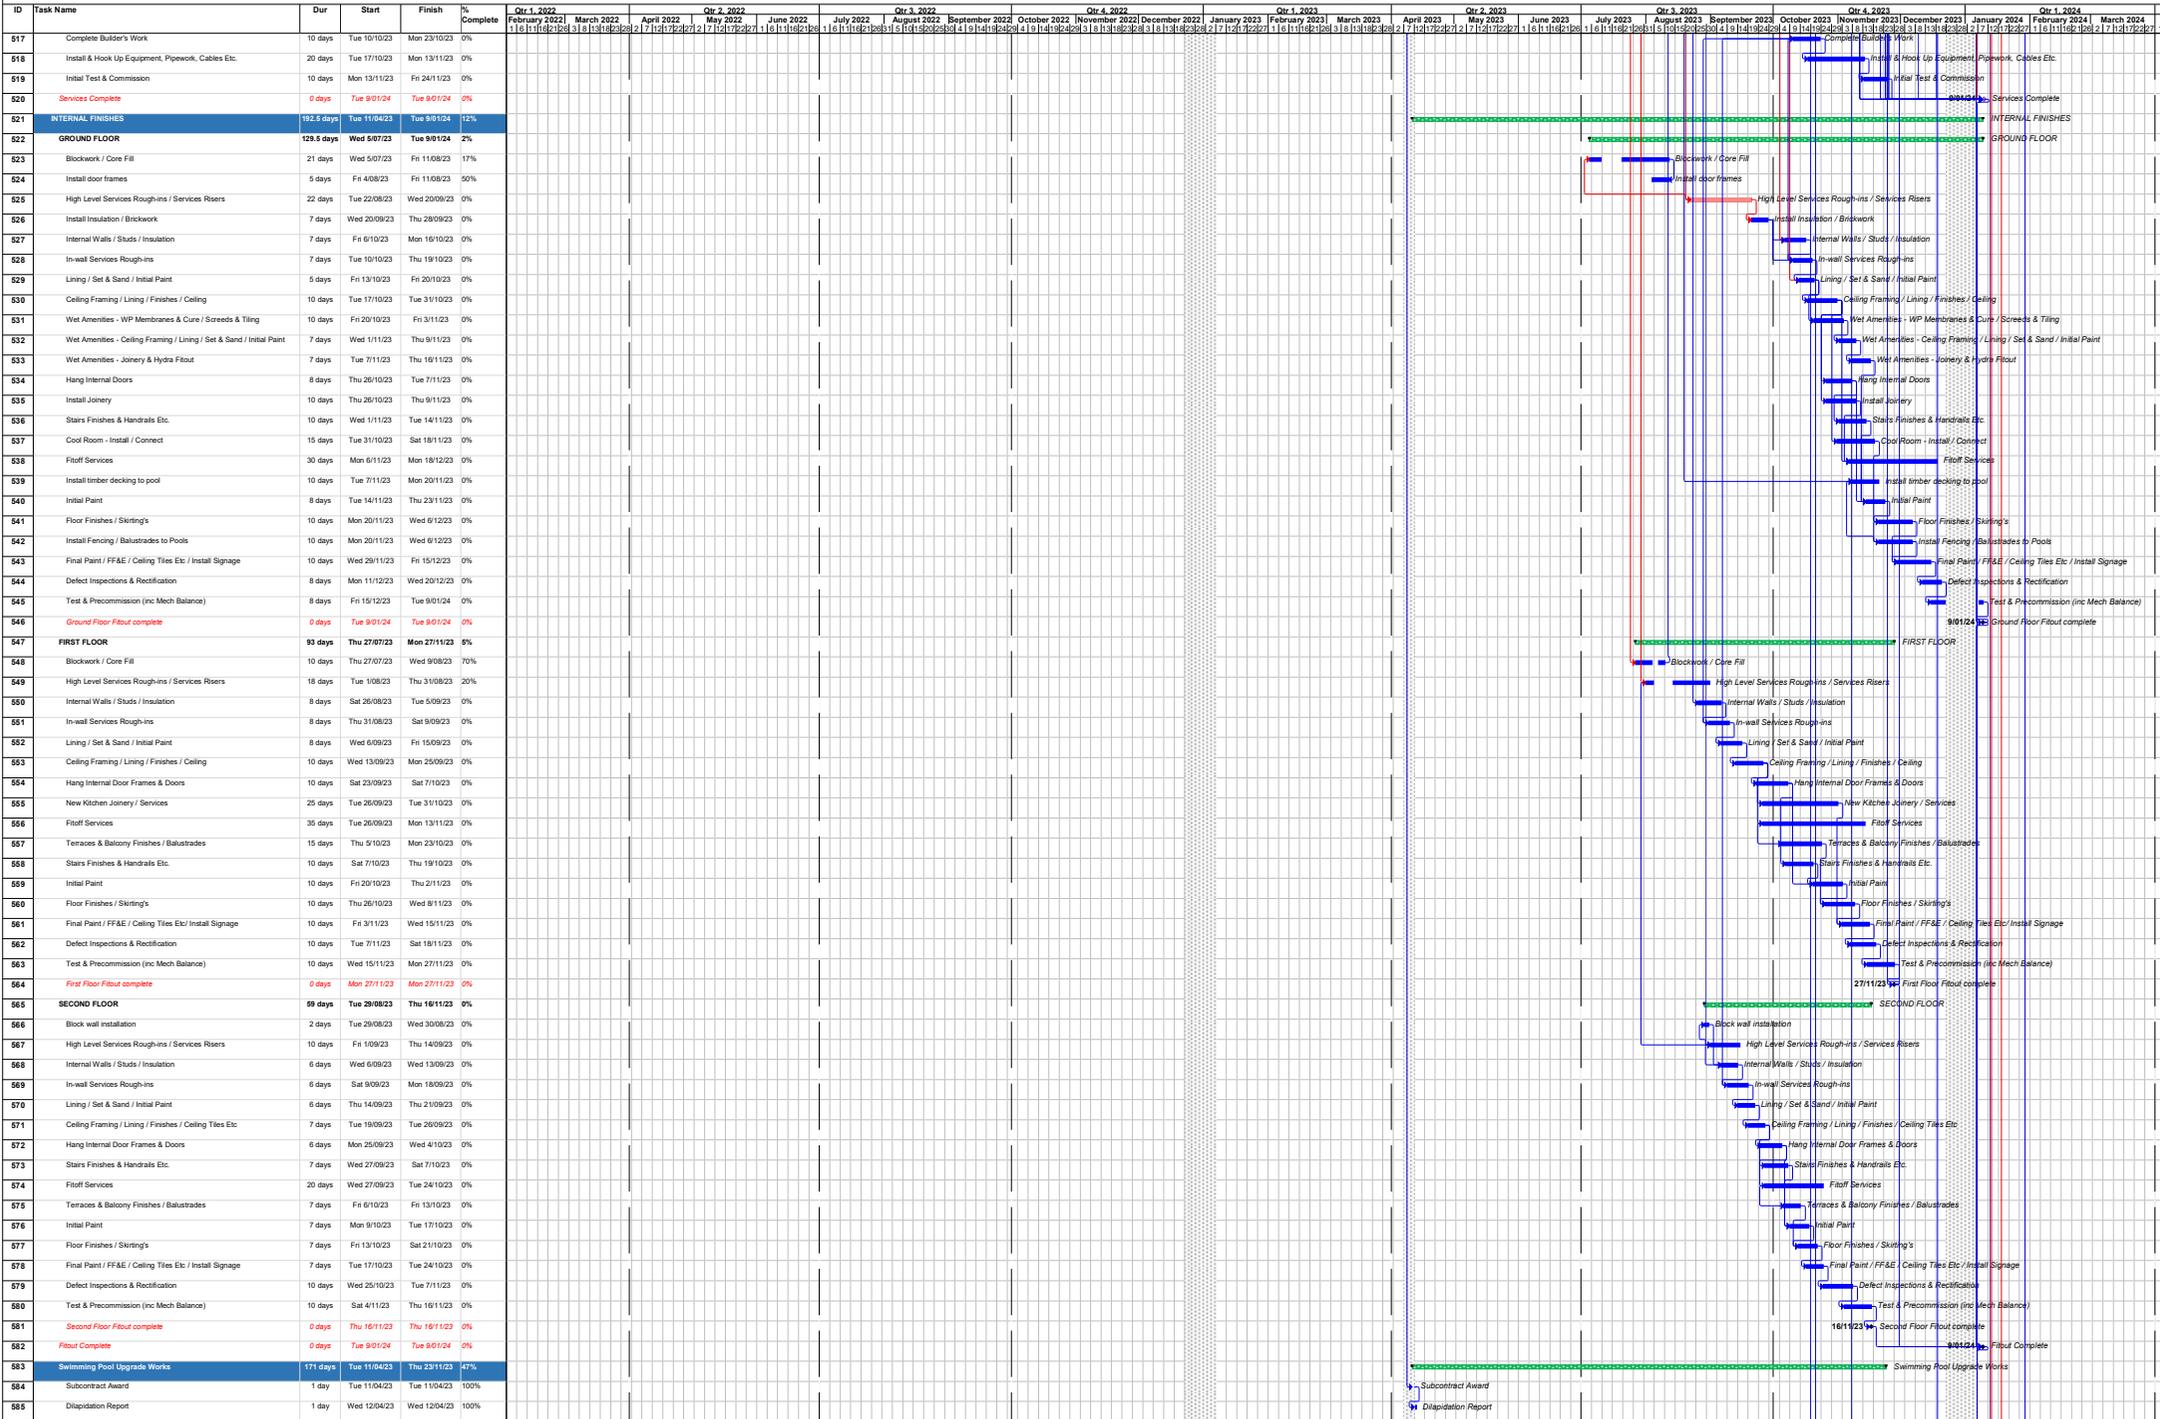



**ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB  
62 PRINCE STREET, CRONULLA NSW 2230  
DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 08 AUGUST 2023**



ID	Task Name	Dur	Start	Finish	In Complete	Qtr 1, 2022		Qtr 2, 2022		Qtr 3, 2022		Qtr 4, 2022		Qtr 1, 2023		Qtr 2, 2023		Qtr 3, 2023		Qtr 4, 2023		Qtr 1, 2024			
						Feb 2022	Mar 2022	Apr 2022	May 2022	Jun 2022	Jul 2022	Aug 2022	Sep 2022	Oct 2022	Nov 2022	Dec 2022	Jan 2023	Feb 2023	Mar 2023	Apr 2023	May 2023	Jun 2023	Jul 2023	Aug 2023	Sep 2023
486	Demolition Works	15 days	Wed 18/04/23	Mon 8/05/23	100%																				
485	Refurbishment Works	116 days	Tue 30/05/23	Tue 31/10/23	38%																				
486	Installation of Epoxy or Cementitious Render to Balance Tank	21 days	Tue 30/05/23	Tue 27/06/23	90%																				
487	Installation of Bonding Slurry, Screed, and Cementitious Render	21 days	Tue 30/05/23	Sat 15/07/23	90%																				
488	Install new Equipotential Earthing	5 days	Thu 17/08/23	Wed 23/08/23	0%																				
489	Install new Lane Dividing Anchors	3 days	Thu 24/08/23	Sat 26/08/23	0%																				
490	Installation of Expansion Joints	1 day	Thu 24/08/23	Thu 24/08/23	0%																				
491	WITNESS AND HOLD POINT 3	1 day	Mon 28/08/23	Mon 28/08/23	0%																				
492	Manufacturer's Inspection and approval	1 day	Tue 29/08/23	Tue 29/08/23	0%																				
493	Carry Out Photo Report	1 day	Wed 30/08/23	Wed 30/08/23	0%																				
494	Installation of Rubber Tape	1 day	Thu 31/08/23	Thu 31/08/23	0%																				
495	Installation of Cementitious Waterproofing	5 days	Fri 1/09/23	Thu 7/09/23	0%																				
496	WITNESS AND HOLD POINT 4	1 day	Fri 8/09/23	Fri 8/09/23	0%																				
497	Manufacturer's Inspection and approval	1 day	Sat 9/09/23	Sat 9/09/23	0%																				
498	Carry out Photo Report	1 day	Tue 12/09/23	Tue 12/09/23	0%																				
499	WITNESS AND HOLD POINT 5	1 day	Wed 13/09/23	Wed 13/09/23	0%																				
500	Installation of Fibre Glass Mesh	3 days	Thu 14/09/23	Mon 18/09/23	0%																				
501	Installation of Adhesives and Tiles	15 days	Tue 19/09/23	Mon 9/10/23	0%																				
502	Installation of Grout	10 days	Tue 10/10/23	Sat 21/10/23	0%																				
503	Manufacturer's Inspection and approval	1 day	Mon 23/10/23	Mon 23/10/23	0%																				
504	Installation of new Return Line Nozzle Covers	1 day	Tue 24/10/23	Tue 24/10/23	0%																				
505	Painting of Pool Wall Exterior	4 days	Tue 24/10/23	Fri 27/10/23	0%																				
506	Installation of new Statutory Signage	1 day	Tue 31/10/23	Tue 31/10/23	0%																				
507	Refurbishment Completion Date	0 days	Tue 31/10/23	Tue 31/10/23	0%																				
508	Swimming Pool Completion Date and Hand Over	19 days	Wed 11/11/23	Thu 23/11/23	0%																				
509	Final Clean	3 days	Wed 11/11/23	Fri 11/11/23	0%																				
510	Builder's Inspection and Approval	1 day	Sat 4/11/23	Sat 4/11/23	0%																				
511	Final Inspection Date	0 days	Sat 4/11/23	Sat 4/11/23	0%																				
512	Photo Report	1 day	Mon 6/11/23	Mon 6/11/23	0%																				
513	Demolition	1 day	Tue 7/11/23	Tue 7/11/23	0%																				
514	Warranties	1 day	Wed 8/11/23	Wed 8/11/23	0%																				
515	Certification	1 day	Wed 8/11/23	Wed 8/11/23	0%																				
516	Confirm Maintenance Programme	1 day	Wed 8/11/23	Wed 8/11/23	0%																				
517	Practical Completion (NETT)	0 days	Wed 8/11/23	Wed 8/11/23	0%																				
518	Inclement Weather Allowance	12 days	Thu 9/11/23	Thu 23/11/23	0%																				
519	Practical Completion (GROSS)	0 days	Thu 23/11/23	Thu 23/11/23	0%																				
520	EXTERNAL WORKS / PUBLIC DOMAIN	44 days	Sat 21/10/23	Thu 12/12/23	0%																				
521	Start External Works after Scaffold Down & Facade Complete	0 days	Sat 21/10/23	Sat 21/10/23	0%																				
522	Run Remaining Inground Services / Pits / Backfill	10 days	Mon 23/10/23	Sat 4/11/23	0%																				
523	Hard Landscaping / Pavement / Crossover / Kerbs & Edges / Garden Beds, Gates Etc	20 days	Fri 27/10/23	Wed 22/11/23	0%																				
524	Soft Landscaping / Planting	20 days	Fri 10/11/23	Fri 8/12/23	0%																				
525	Signage / External FF & E / Handrails / Make Good	10 days	Thu 30/11/23	Fri 15/12/23	0%																				
526	Defect Inspections & Rectification	10 days	Mon 11/12/23	Thu 21/12/23	0%																				
527	External Works Complete	0 days	Thu 21/12/23	Thu 21/12/23	0%																				
528	COMPLETION OF WORKS & HANDOVER	20 days	Mon 8/01/24	Thu 1/02/24	0%																				
529	Commence Final Commissioning after Fitout & Services Complete	0 days	Tue 9/01/24	Tue 9/01/24	0%																				
530	Handover Manuals / As-Built Documentation / Certificates / Keys	5 days	Wed 10/01/24	Mon 15/01/24	0%																				
531	Inspections & Obtain Interim Certificate of Occupancy	7 days	Mon 8/01/24	Mon 15/01/24	0%																				
532	Final Staff Training	7 days	Mon 8/01/24	Mon 15/01/24	0%																				
533	Remove Hoardings / Builders Demobilise	7 days	Mon 8/01/24	Mon 15/01/24	0%																				
534	Overall Commissioning & Handover complete	0 days	Mon 15/01/24	Mon 15/01/24	0%																				
535	Practical Completion (NETT)	0 days	Mon 15/01/24	Mon 15/01/24	0%																				
536	Inclement Weather Allowance	12 days	Tue 16/01/24	Wed 31/01/24	0%																				
537	Practical Completion (GROSS)	0 days	Thu 1/02/24	Thu 1/02/24	0%																				
538	EXTENSIONS OF TIME	331 days	Tue 3/05/22	Mon 7/08/23	100%																				
539	May 2022 - Asbestos discovery, management and remediation (Approved)	22 days	Tue 3/05/22	Tue 31/05/22	100%																				
540	June 2022 - Asbestos discovery, management and remediation (Approved)	21 days	Wed 1/06/22	Thu 30/06/22	100%																				
541	July 2022 - Asbestos discovery, management and remediation (Approved)	23 days	Fri 1/07/22	Sat 30/07/22	100%																				
542	Feb 2023 - Inclement Weather Event (time Claim only)	1 day	Tue 14/02/23	Tue 14/02/23	100%																				
543	March 2023 - Inclement Weather Event (time Claim only)	1 day	Tue 14/03/23	Tue 14/03/23	100%																				
544	August 2023 - Inclement Weather Event (time Claim only)	1 day	Mon 7/08/23	Mon 7/08/23	100%																				
