




ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023

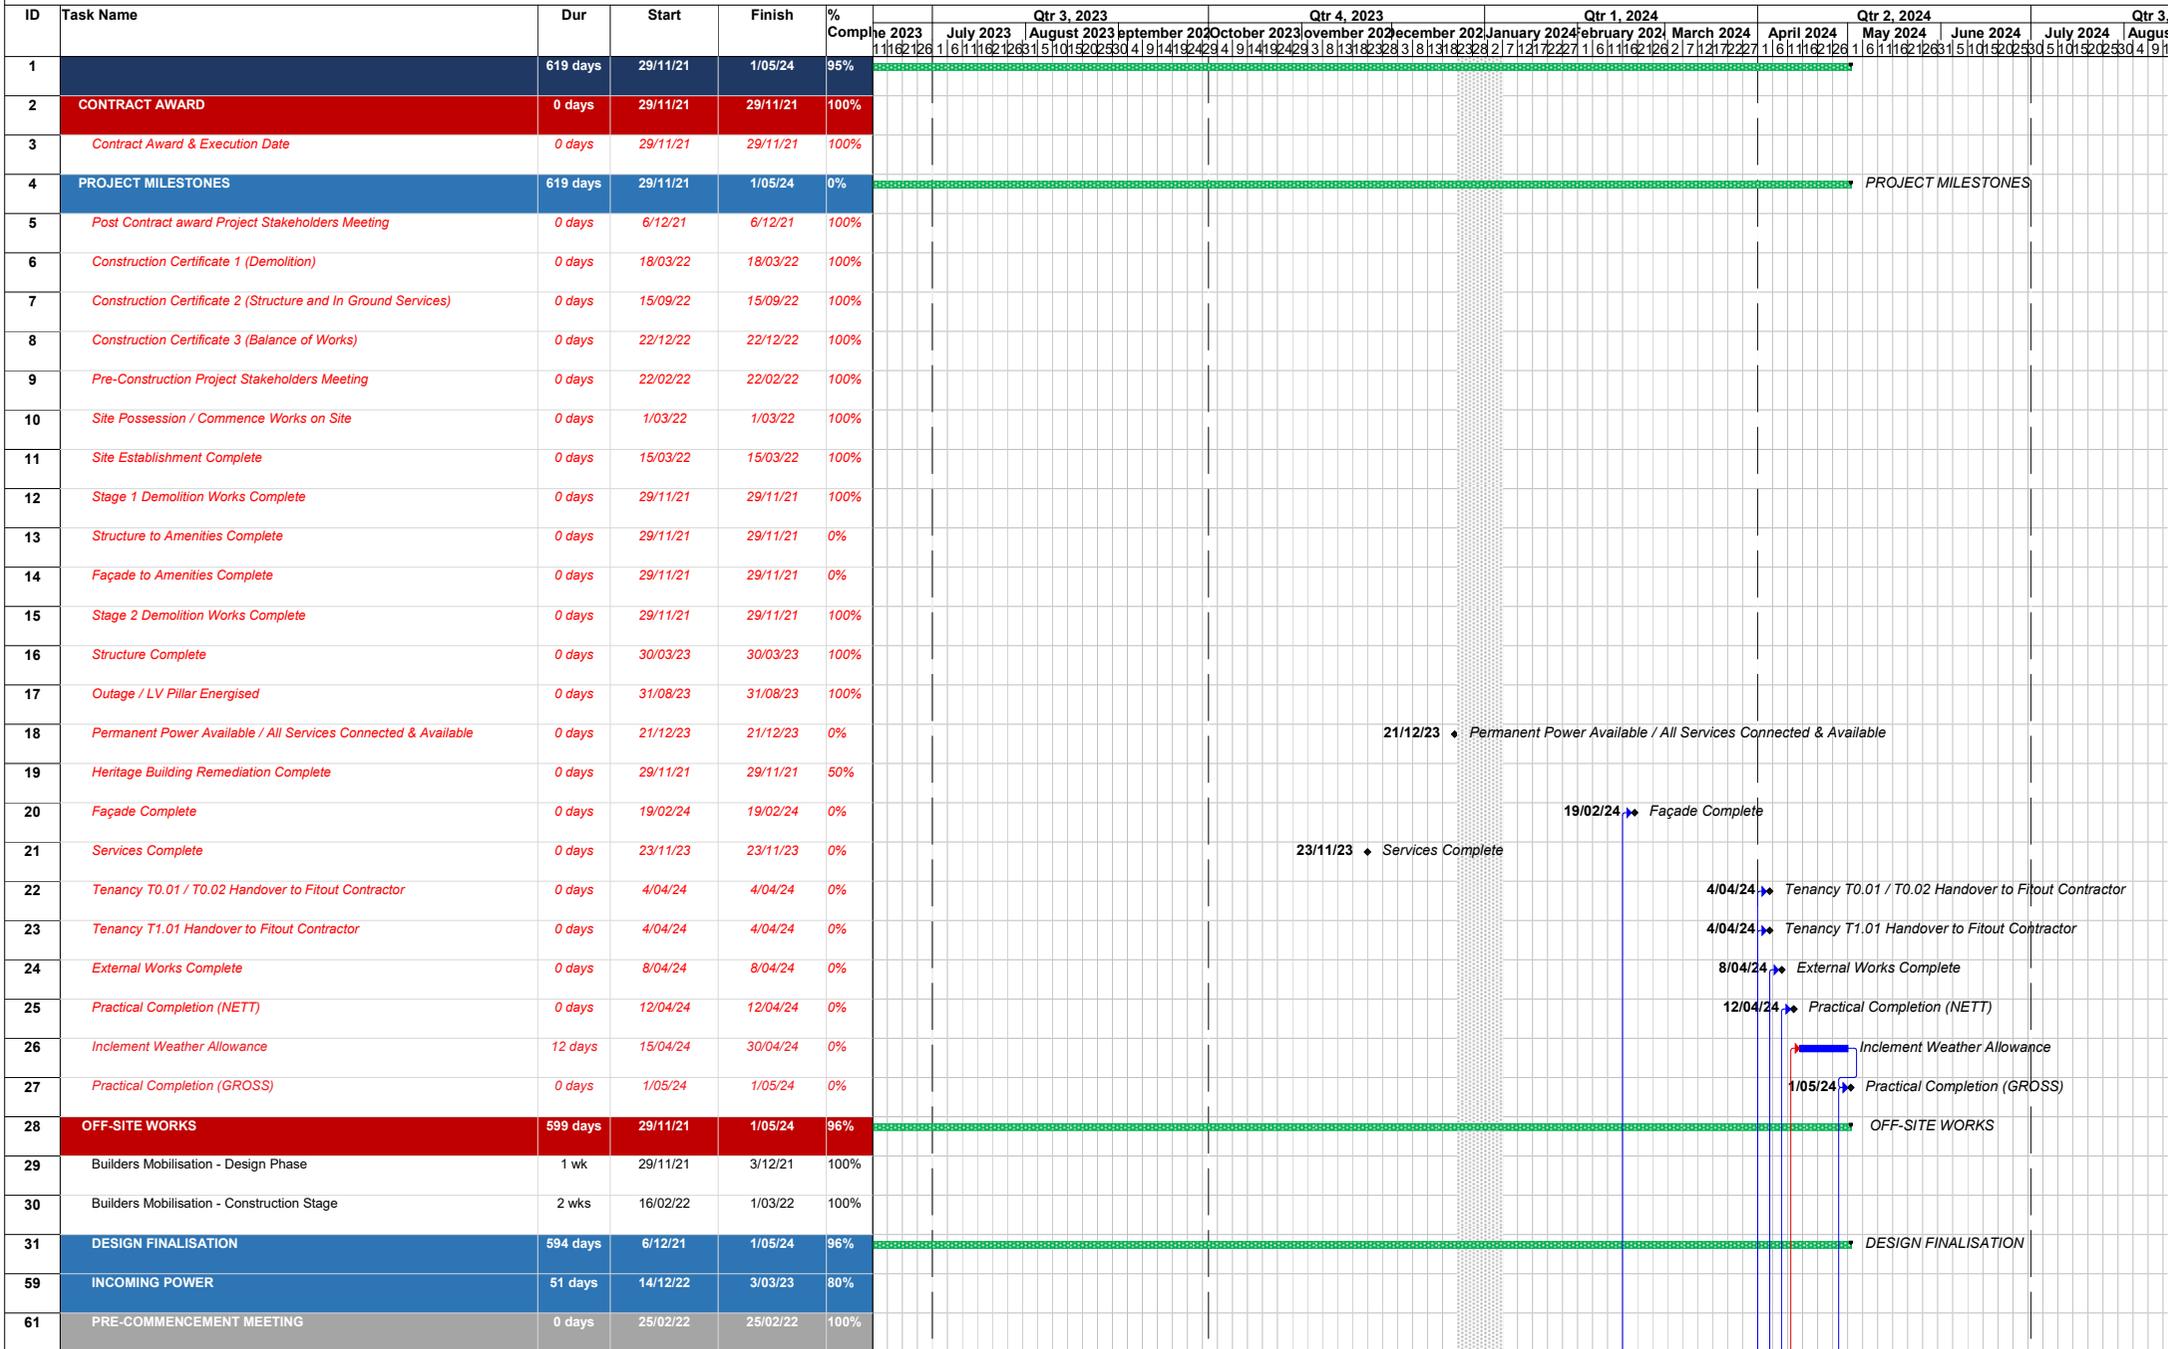

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas

----- Critical Split
 ----- Critical Task
 ----- Milestone
 ----- Non-Critical Task
 ----- Summary
 ----- Project Summary
 ----- Path Successor Summary Task
 ----- Path Successor Milestone Task
 ----- Critical
 ----- Critical



ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023



ID	Task Name	Dur	Start	Finish	% Complete	Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024					
						July 2023	August 2023	September 2023	October 2023	November 2023	December 2023	January 2024	February 2024	March 2024	April 2024	May 2024	June 2024	July 2024	August 2024				
63	MANAGEMENT PLANS	27 days	14/01/22	22/02/22	100%																		
77	AUTHORITY APPROVALS	410 days	29/11/21	26/07/23	97%	AUTHORITY APPROVALS																	
78	CONSTRUCTION CERTIFICATE 1 (CC1) - DEMOLITION	28 days	9/02/22	18/03/22	100%																		
83	CONSTRUCTION CERTIFICATE 2 (CC2) - Piling, Ground Floor Slab and In Ground Services	10 days	2/09/22	15/09/22	100%																		
88	CONSTRUCTION CERTIFICATE 3 (CC3) - Fitout and services	24 days	21/11/22	22/12/22	100%																		
93	SITE MANAGEMENT PLAN	21 days	14/12/21	19/01/22	100%																		
97	LV PILLAR	78 days	31/03/23	24/07/23	90%	LV PILLAR																	
103	PARKSIDE LIGHTING	344 days	10/03/22	26/07/23	98%	PARKSIDE LIGHTING																	
107	SECTION 73	0 days	29/11/21	29/11/21	100%																		
109	SUBCONTRACT LETTING (KEY TRADES)	437 days	6/12/21	8/09/23	95%	SUBCONTRACT LETTING (KEY TRADES)																	
178	PRELIMINARIES	549 days	2/03/22	12/04/24	99%	PRELIMINARIES																	
179	TEMPORARY FENCE/ HOARDING	549 days	2/03/22	12/04/24	0%	TEMPORARY FENCE/ HOARDING																	
182	SCAFFOLDING IN-USE	213 days	14/03/23	11/01/24	100%	SCAFFOLDING IN-USE																	
183	Set Up Scaffolding	0 days	14/03/23	14/03/23	100%																		
184	Façade Complete	0 days	24/10/23	24/10/23	100%																		
185	Remove Scaffolding	3 days	9/01/24	11/01/24	100%	Remove Scaffolding																	
186	ON-SITE WORKS	619 days	29/11/21	1/05/24	58%	ON-SITE WORKS																	
187	SITE ESTABLISHMENT	516 days	1/03/22	28/02/24	83%	SITE ESTABLISHMENT																	
188	Site Possession / Commence Works on Site	0 days	1/03/22	1/03/22	100%																		
189	Club Handover to Builder	0 days	1/03/22	1/03/22	100%																		
190	Site Establishment - Erect Temporary Hoardings, Directional Signages Etc.	5 days	2/03/22	8/03/22	100%																		
191	Create Site Access Points / Pedestrian Protection / Associated Works / Modify Street Parking	2 days	9/03/22	10/03/22	100%																		
192	Initial Site Set-up & Temporary Site Services	5 days	9/03/22	14/03/22	100%																		
193	Setup Temporary Accommodation and Amenities	5 days	9/03/22	14/03/22	100%																		
194	Install Tree Protection / Trim Trees	1 day	14/04/22	14/04/22	100%																		
195	Install Tiger Tails to Existing Overhead Power	1 day	11/03/22	11/03/22	100%																		
196	Erect Perimeter Hoardings to Building / Protect Heritage Façade	8 days	9/03/22	17/03/22	100%																		
197	Decommissioning Of Pool / Removal of Equipment / Drain Pool / Safety Handrail	6 days	9/03/22	15/03/22	100%																		
198	DEMOLITION WORKS	139 days	24/03/22	30/09/22	100%																		
213	CIVIL WORKS	66 days	19/07/22	13/10/22	100%																		

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas

● Critical Split
■ Critical Task
● Non-Critical Task
■ Milestone
■ Summary
◆ Project Summary
■ Path Successor Summary Task
◆ Path Successor Milestone Task
■ Critical
◆


Revision: 00 Check: SM Approved: SS



ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023

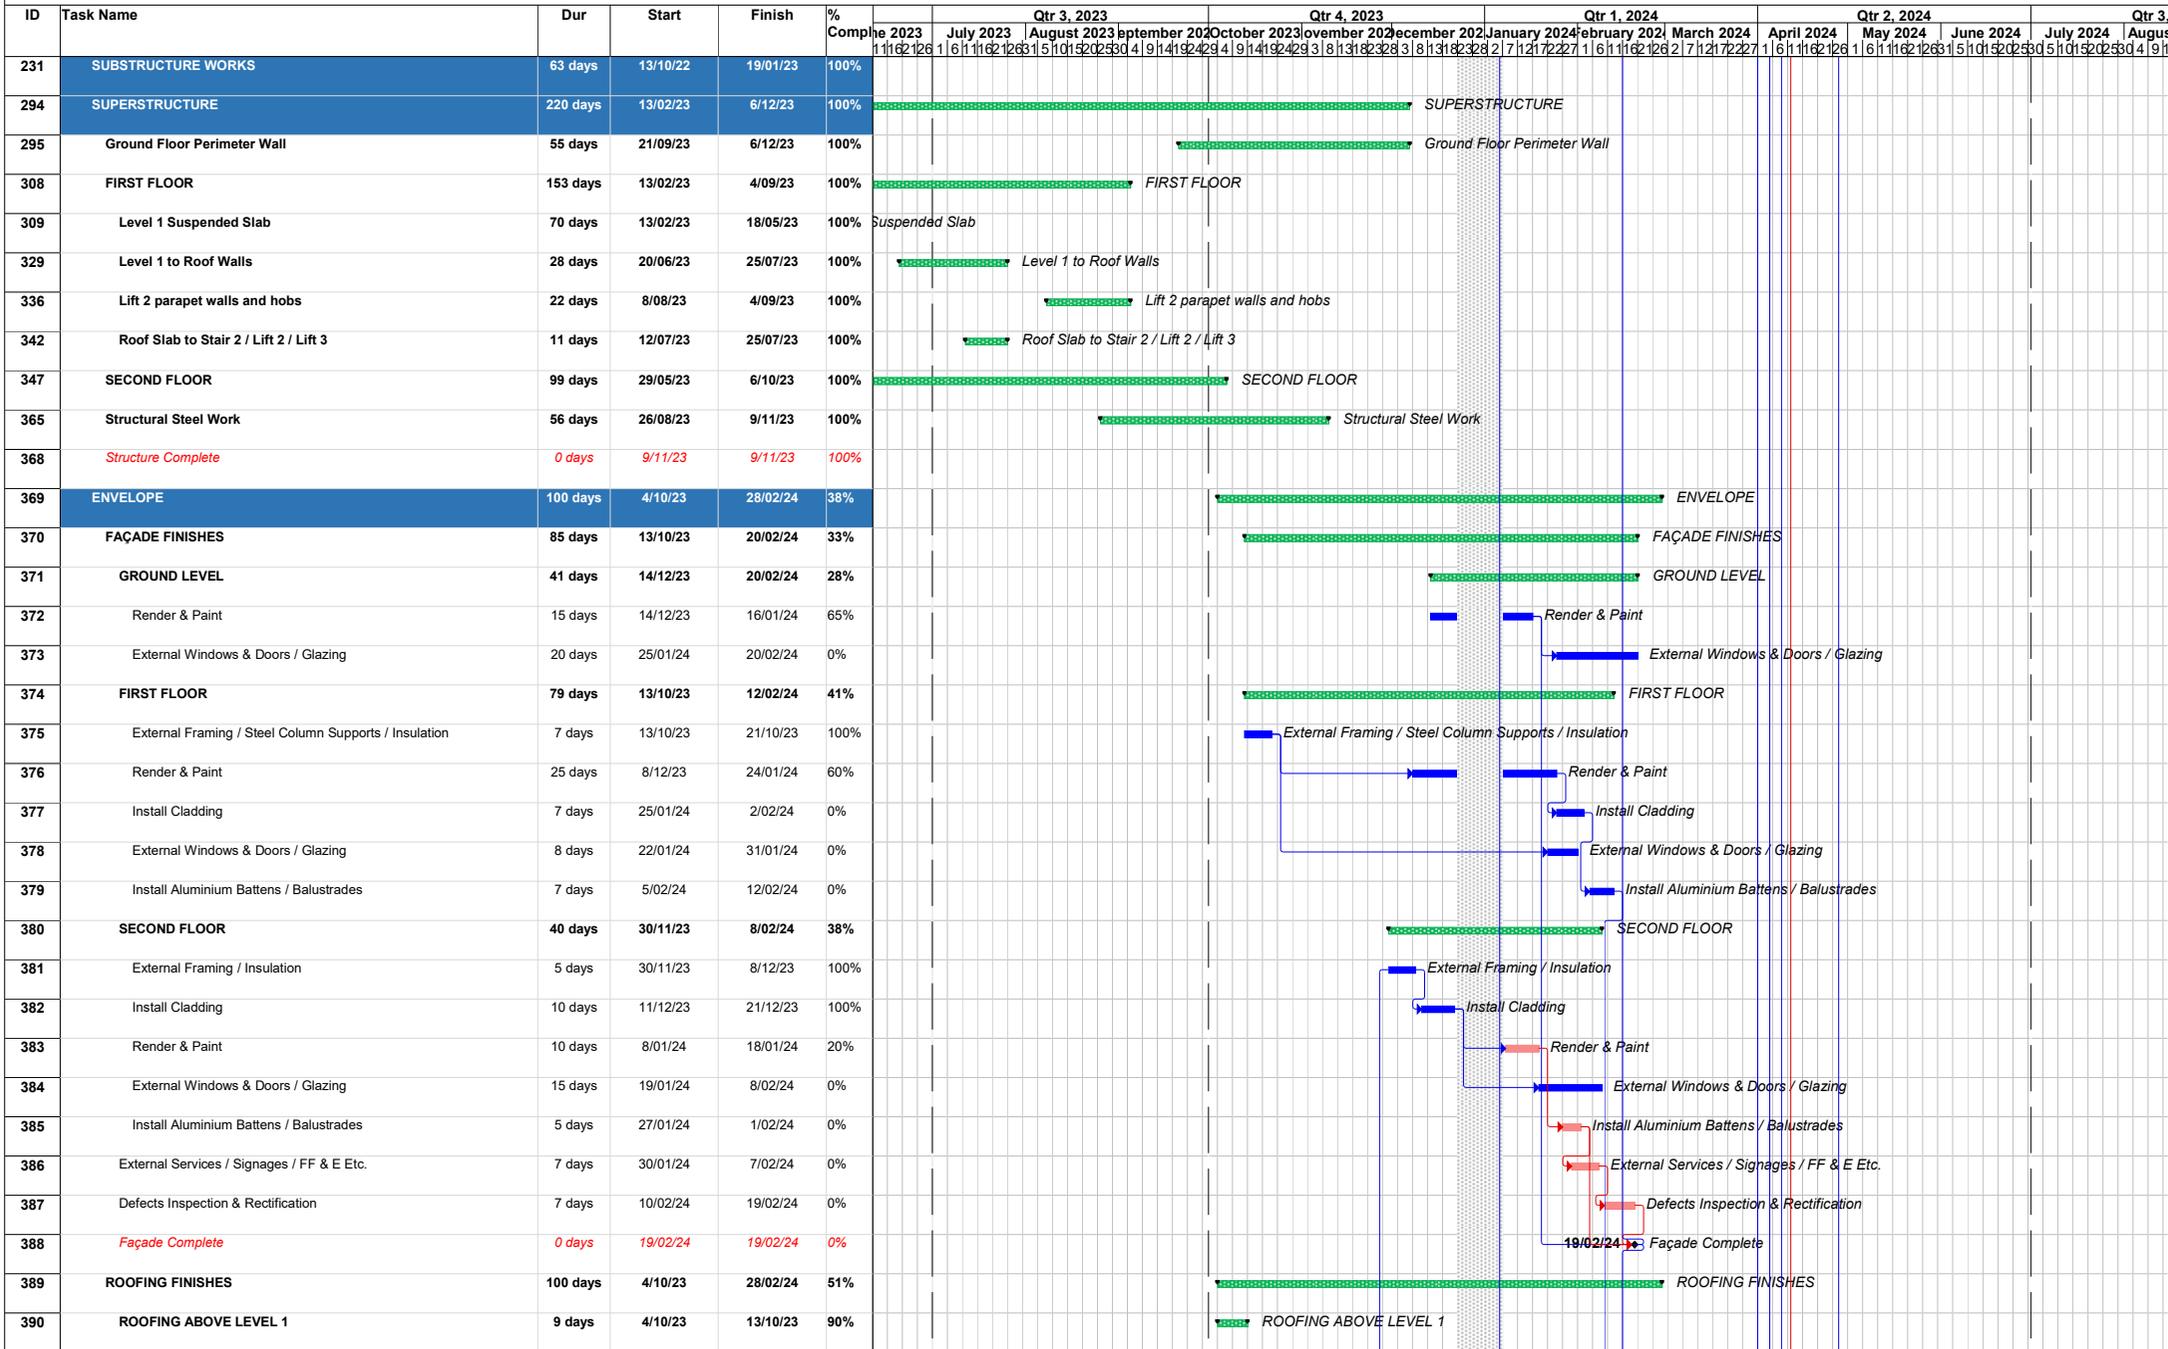

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas


..... Critical Split
 Non-Critical Task
 Summary
 Path Successor Summary Task
 Critical
■ Critical Task
 ■ Milestone
 ◆ Project Summary
 ◆ Path Successor Milestone Task
 ◆



ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023

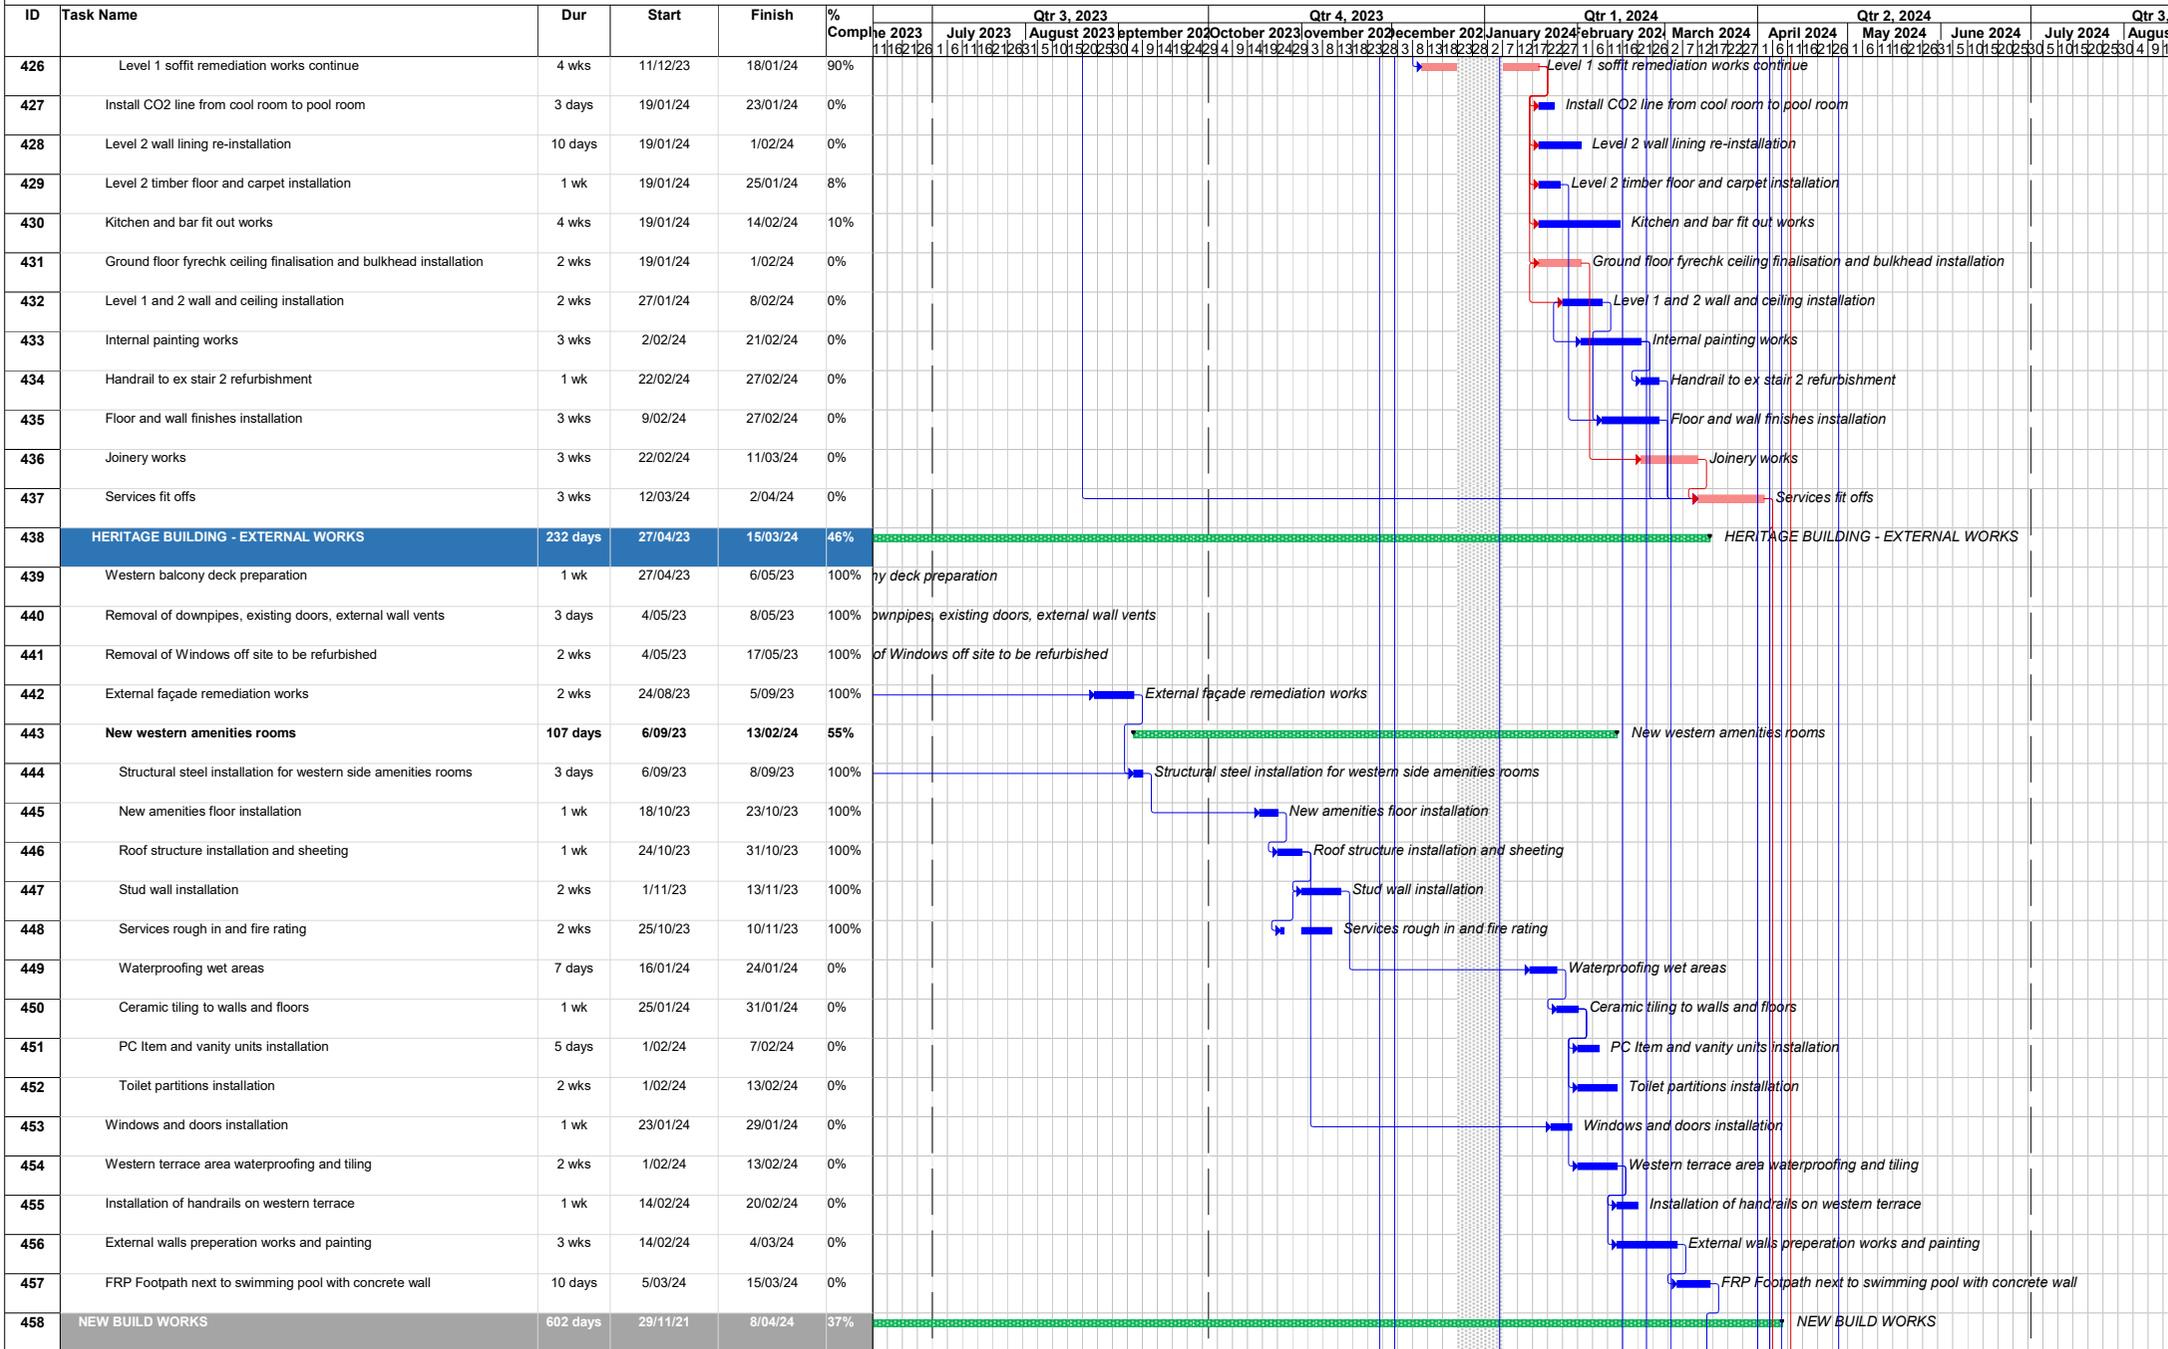

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas


----- Critical Split
----- Critical Task
----- Non-Critical Task
----- Milestone
----- Summary
----- Project Summary
----- Path Successor Summary Task
----- Path Successor Milestone Task
----- Critical



ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023

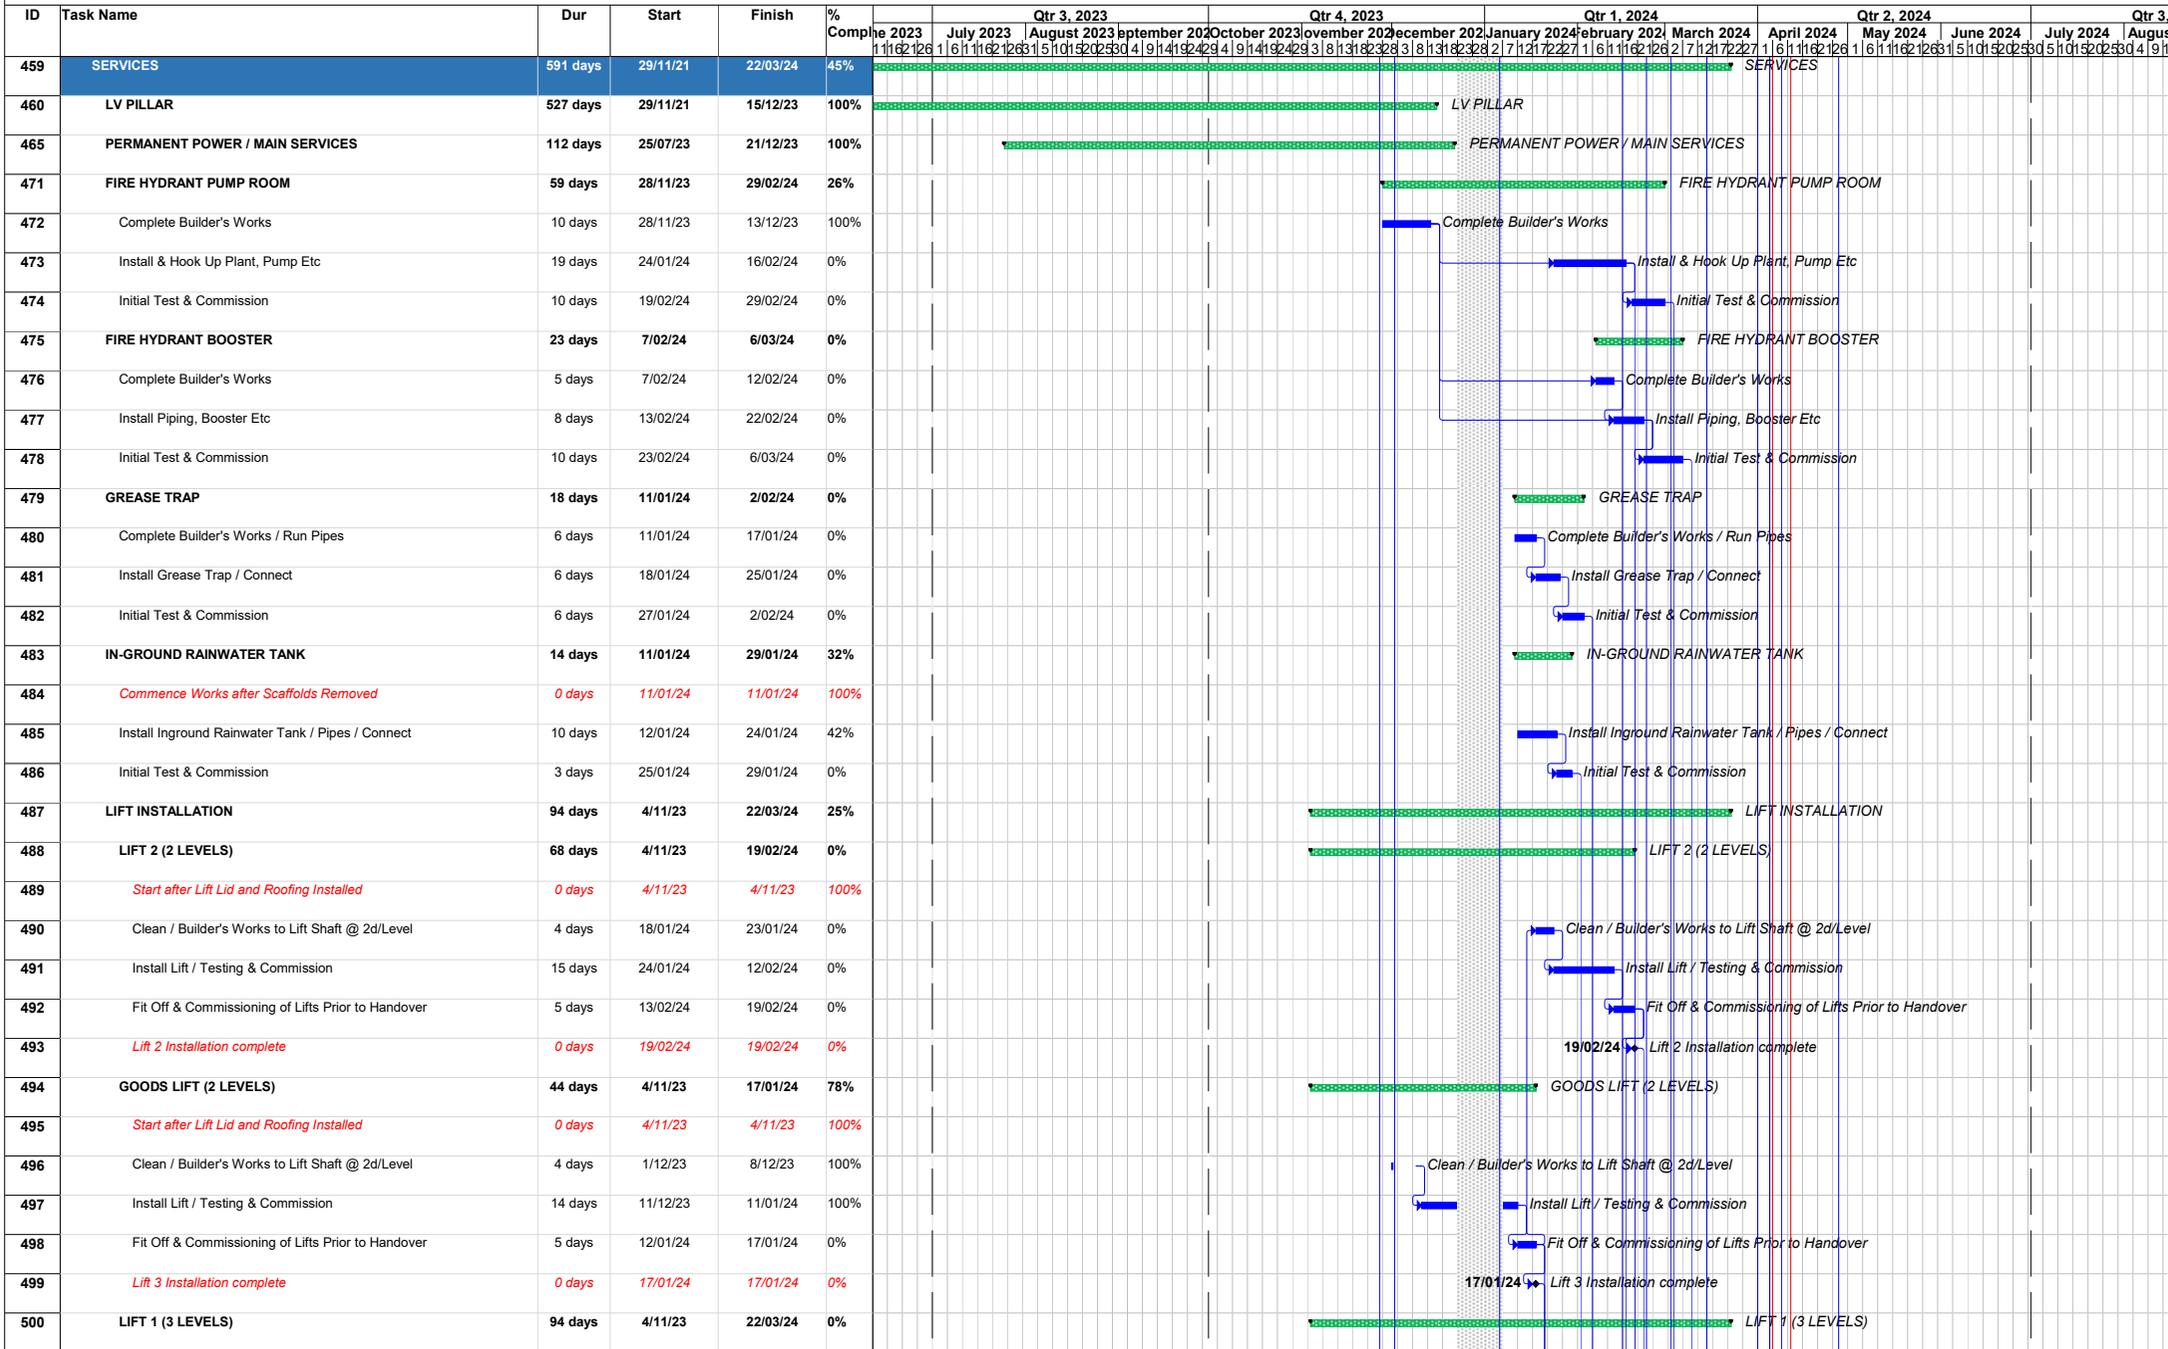

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas


----- Critical Split
 ----- Critical Task
 ----- Non-Critical Task
 ----- Milestone
 ----- Summary
 ----- Project Summary
 ----- Path Successor Summary Task
 ----- Path Successor Milestone Task
 ----- Critical



ALTERATIONS AND ADDITIONS TO NORTH CRONULLA SURF LIFE SAVING CLUB

62 PRINCE STREET, CRONULLA NSW 2230

DESIGN & CONSTRUCT - CONSTRUCTION PROGRAM ISSUED 15 JANUARY 2023

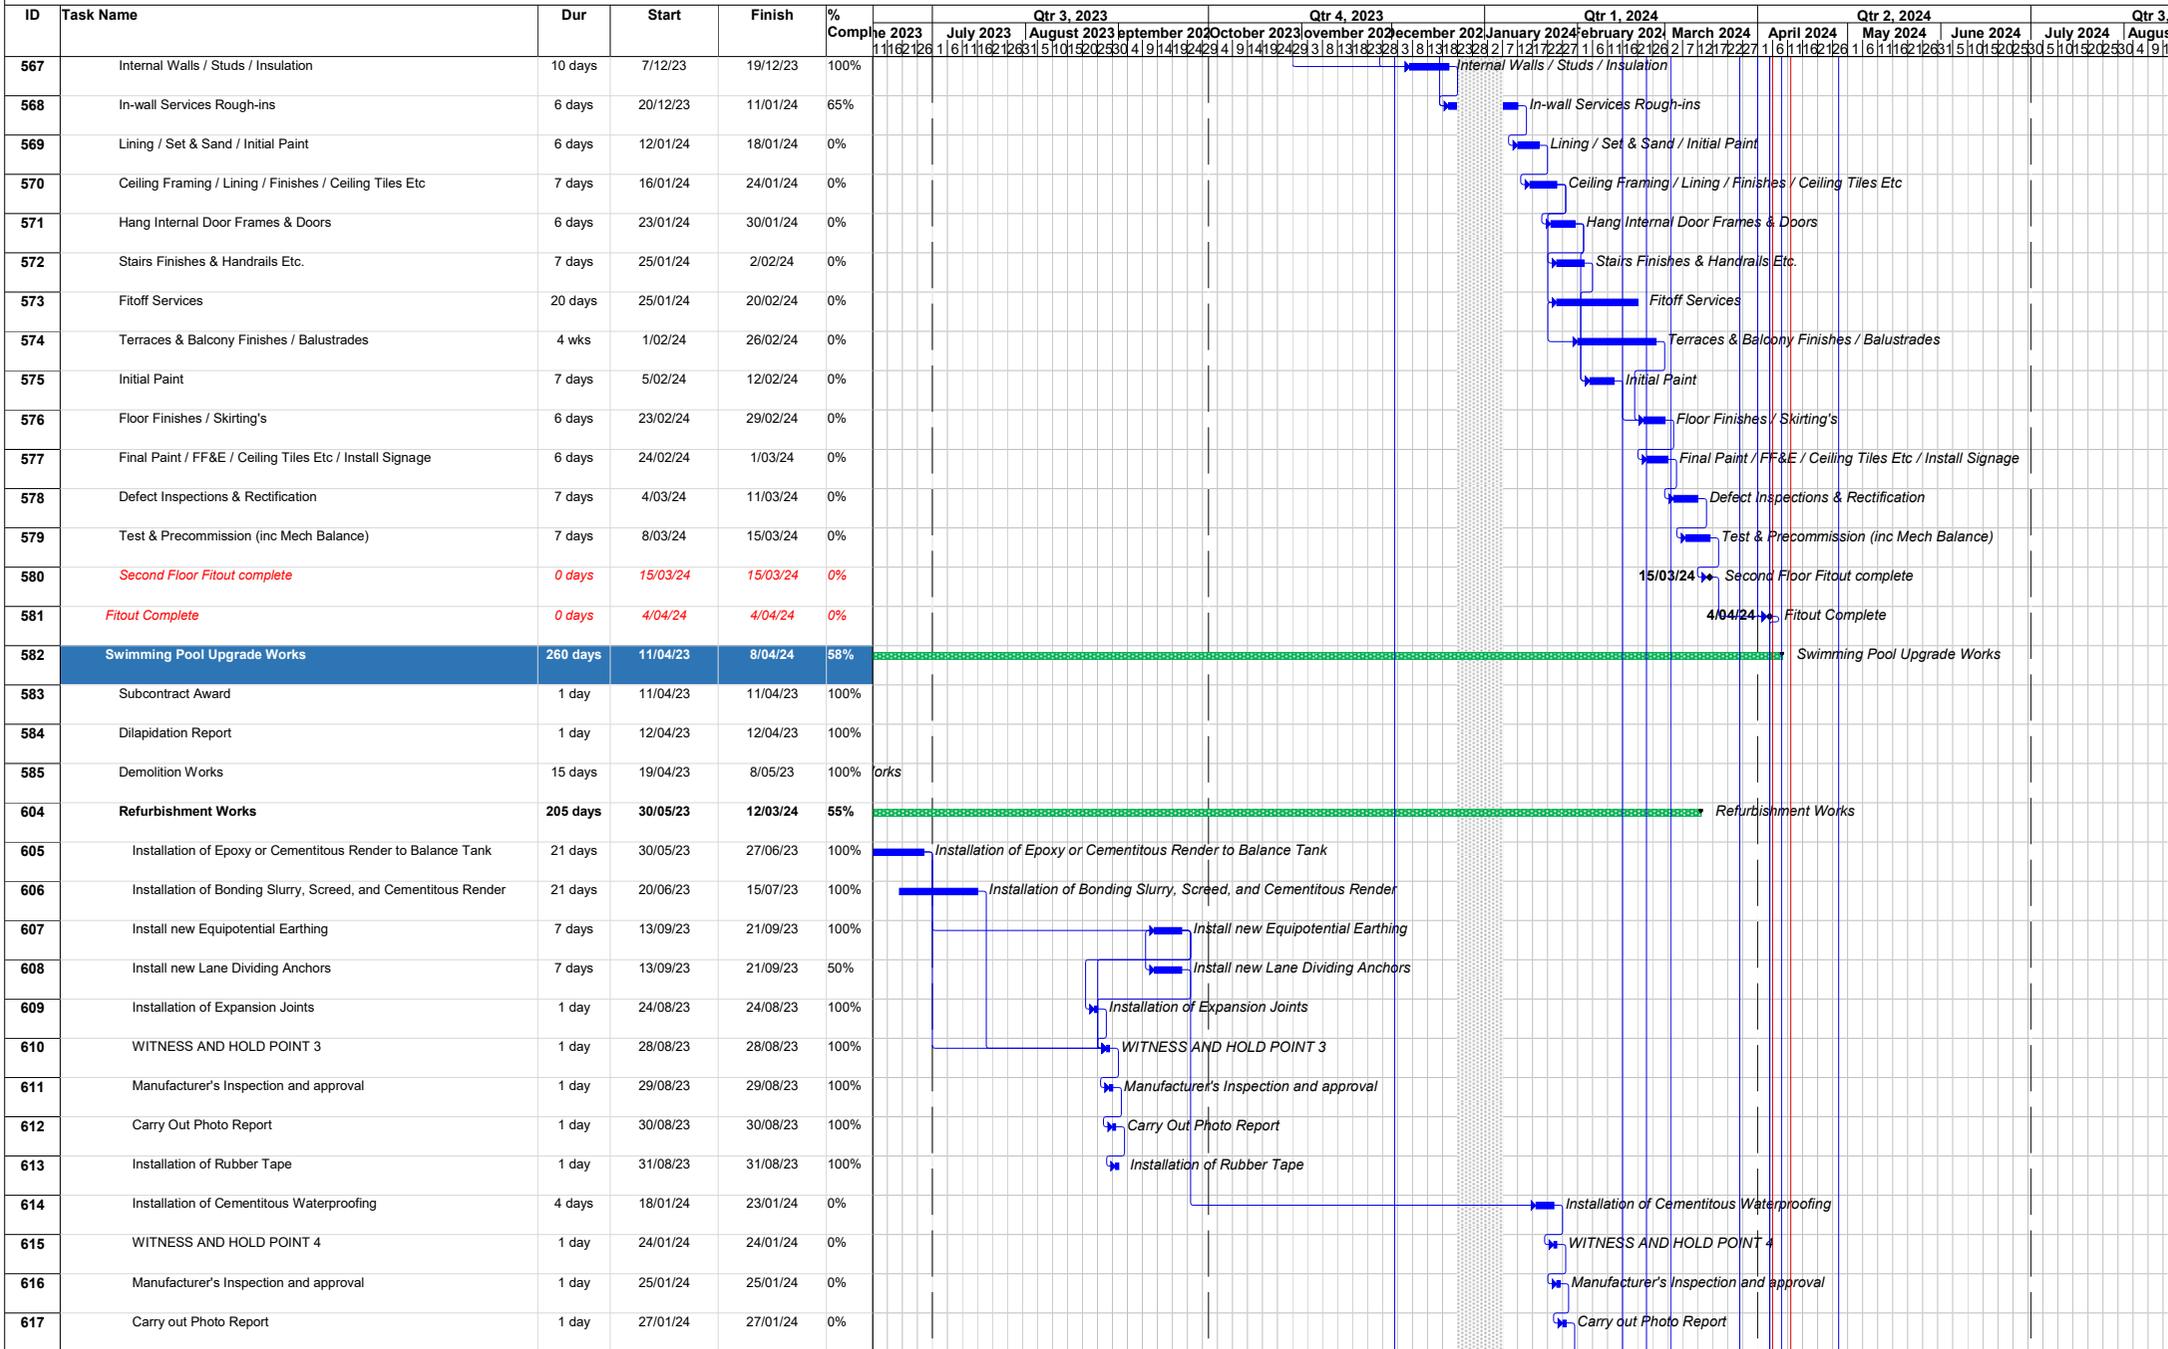

The Programme is based on a 5.5-day working week incl. of RDO's, PH & Xmas

----- Critical Split
----- Critical Task
----- Non-Critical Task
----- Milestone
----- Summary
----- Project Summary
----- Path Successor Summary Task
----- Path Successor Milestone Task
----- Critical
